

ANTRAC HOLDING PVT LTD
Well Land Investment Pvt Ltd

STRATEGIC INNOVATION & TRANSFORMATION ROADMAP

A Board Advisory Report on Building a High-Performance, Future-Ready Operations Model

Prepared by	Ali Mushthaq Ibrahim
Role	General Manager — Logistics (Well Land Operations)
Presented to	Board of Directors, Antrac Holding Pvt Ltd
Date	March 2026
Classification	CONFIDENTIAL — For Board Use Only

CONFIDENTIALITY NOTICE

This report has been prepared for the exclusive use of the Board of Directors of Antrac Holding Pvt Ltd. The contents of this document, including all strategic recommendations, financial analyses, operational frameworks, and supporting data, are confidential and proprietary to Well Land Investment Pvt Ltd and Antrac Holding Pvt Ltd. Distribution, reproduction, or disclosure to any third party without prior written consent is strictly prohibited.

The recommendations contained herein are based on operational assessment, industry analysis, and established management frameworks. They are intended to inform board-level decision-making and should be read in conjunction with management's professional judgement and internal financial data.

EXECUTIVE SUMMARY

Well Land Investment Pvt Ltd operates as one of Antrac Holding’s most strategically positioned subsidiaries, providing heavy machinery and vessel rental services to construction and infrastructure projects across the Maldives. The company’s operational profile — asset-intensive, execution-critical, and directly tied to Antrac’s group revenue — makes it uniquely susceptible to the compounding benefits of structured operational improvement.

This report presents a **three-horizon, 36-month transformation roadmap** recommending that Well Land transition from an informally managed operation to a structured, data-driven, and digitally enabled service leader in the Maldivian market. The roadmap is grounded in both the operational realities of Well Land’s current state and in internationally established frameworks for innovation management, performance measurement, and organisational transformation.

The central argument is straightforward: Well Land's competitive advantage over the coming decade will not be determined by fleet size alone, but by its ability to deliver reliable, transparent, and measurable service at pace. That capability must be built deliberately — through formalised processes, real-time data, and a culture of continuous improvement — and it must be built now, before competitive pressure forces reactive rather than strategic change.

KEY FINDINGS & RECOMMENDATIONS	
Strategic Imperative	Antrac's growth ambitions require a Well Land that can scale reliably — informal operations are the primary growth constraint
Critical Gap	No formalised SOPs, KPI tracking, asset readiness framework, or governance reporting structure currently exists
Horizon 1 Priority (0-6M)	Build the operational backbone: SOPs, KPI registers, asset readiness checklists, governance and reporting framework
Horizon 2 Priority (6-18M)	Digitalise and instrument: fleet telematics, condition-based maintenance, digital dispatch and documentation
Horizon 3 Priority (18-36M)	Achieve market leadership: outcome-based contracts, customer co-design, premium brand positioning
Primary Board Action	Endorse and resource the H1 programme; adopt KPI dashboard as standard board reporting instrument

1. Company Profile & Strategic Context

1.1 About Well Land Investment Pvt Ltd

Well Land Investment Pvt Ltd was established in 2014 as a specialist subsidiary within the Antrac Holding Group, created to strengthen Antrac’s capabilities in heavy vehicle rental, marine asset operations, and logistics services. The company provides a critical operational backbone to the Maldivian construction and infrastructure sector, supplying cranes, excavators, high-capacity trailers, barges, tugboats, and associated certified operators for projects of all scales across the archipelago.

Figure 1: Well Land Investment — Company Profile

WELL LAND INVESTMENT PVT LTD — COMPANY PROFILE	
Parent Company	Antrac Holding Pvt Ltd — Malé, Republic of Maldives
Established	2014
Sector	Heavy Equipment & Vessel Rental Logistics General Trading
Fleet Assets	Cranes, Excavators, High-Capacity Trailers, Barges, Tugboats
Key Markets Served	Construction, Infrastructure Development, Marine Operations — nationwide across Maldives
Value Proposition	Asset access + certified operators + mobilisation + safety protocols
Reporting Line	Board of Directors, Antrac Holding Pvt Ltd
GM Logistics (Well Land Ops)	Ali Mushthaq Ibrahim — January 2026 to present

Source: Antrac Holding Pvt Ltd (n.d.a, n.d.b, n.d.c)

1.2 The Strategic Position Within Antrac Group

Well Land occupies a unique position within the Antrac portfolio. Unlike the group’s marine services, bunkering, or real estate divisions, Well Land’s revenue is **directly correlated with asset availability and operational reliability**. Every hour of unplanned downtime on a crane or barge is a direct revenue loss event, a client trust event, and a safety exposure event simultaneously. This makes Well Land both the most operationally complex subsidiary in the Antrac Group and the one with the highest potential return on structured improvement investment.

The appointment of a dedicated General Manager — Logistics in January 2026 represents a significant signal of Antrac’s commitment to professionalising Well Land’s operations. This report builds on that strategic intent, translating it into a structured **36-month transformation programme** with defined phases, measurable milestones, and a clear governance framework for board oversight.

2. The Market Imperative — Why This Transformation, Why Now

The Maldivian infrastructure and construction market is entering a sustained expansion cycle, driven by resort development, inter-island connectivity projects, and government infrastructure programmes. This creates a significant growth opportunity for Well Land — but it also raises the competitive stakes. Project owners and main contractors are becoming more sophisticated in their procurement standards, demanding service reliability, digital documentation, and compliance evidence that informal operations cannot consistently provide.

Five converging forces make the **current 12-month window** critical for initiating the transformation. Early-mover advantage in operational formalisation, digital capability, and service reliability is available to Well Land now — but it will not remain available indefinitely as competitors develop or regional operators enter the market.

Table 1: Market Drivers and Well Land Transformation Imperatives

DRIVER	MARKET SIGNAL	WELL LAND IMPLICATION
Digital Disruption	Platform-enabled asset booking and real-time dispatch are becoming industry standard across the region	Without digital dispatch and tracking, Well Land risks appearing operationally opaque to sophisticated project clients
Client Sophistication	Infrastructure project owners and main contractors increasingly mandate digital documentation, uptime SLAs and compliance evidence	Current informal processes create liability exposure and limit access to premium, high-value contracts
IoT & Telematics	Condition-based maintenance via engine-hour tracking, fault-code monitoring and fuel analytics is now commercially accessible at SME scale	Reactive maintenance costs Well Land both revenue (downtime) and reputation — predictive systems are a direct margin lever
Competitive Pressure	Regional plant-hire operators are investing in governance, SOPs, and service reliability as differentiators beyond price	First-mover advantage is available to Well Land in the Maldivian heavy equipment sector — but the window is finite
Antrac Group Ambition	Antrac's portfolio growth across marine services, logistics and real estate demands a Well Land that can scale reliably and safely	An informal, undocumented operation cannot scale — governance and systems must precede growth

Source: Author's operational assessment; Tidd et al. (2021)²; Barney (1991)¹

3. Current State Assessment — Gap Analysis

The following gap assessment is based on direct operational observation since January 2026. It maps Well Land’s current operational state across six critical dimensions against the target state required to execute the transformation programme. The gaps identified are not failures — they reflect **the natural starting point of a 12-year-old operation that grew without a dedicated management layer**. They are, however, gaps that must be closed systematically in Horizon 1 before any Horizon 2 or Horizon 3 investment will deliver its intended return.

Table 2: Current State vs Target State — Gap Assessment

DIMENSION	CURRENT STATE	TARGET STATE	GAP / RISK
Operational SOPs	Informal, undocumented — dependent on individual operator knowledge	Standardised, documented, version-controlled procedures for all asset classes	Single point of failure; no auditability; onboarding risk
KPI & Performance Tracking	No formalised tracking system; performance assessed informally	Live KPI register: utilisation %, uptime, mobilisation time, incident rate	Inability to identify trends, justify investment, or demonstrate value to board
Asset Readiness	Reactive maintenance; no structured pre-mobilisation protocol	Condition-based maintenance schedule; digital pre-start checklists	Unplanned downtime; revenue loss; client trust erosion
Governance & Reporting	Minimal formal reporting to Antrac board; no structured governance layer	Monthly operational dashboard; clear escalation framework; board-level KPI reporting	Board visibility limited; strategic decisions made without data
Fleet Data & Technology	No telematics; no digitalised dispatch; paper-based documentation	IoT-enabled fleet monitoring; digital dispatch; cloud documentation	No predictive capability; high administrative overhead; data blind spots
Service Positioning	Time-based hire only; undifferentiated from competitors on service quality	Outcome-based contracts; premium reliability positioning; client partnerships	Price-only competition; margin pressure; no long-term client lock-in

Source: Operational assessment, Well Land Investment Pvt Ltd, January–March 2026; Neely et al. (1995)⁴; Bititci et al. (2012)⁴

The most critical observation from this assessment is the interdependency of the gaps. The absence of KPI tracking means there is no data to justify technology investment. The absence of SOPs means there is no governance foundation for digital systems to enforce. The absence of governance reporting means the board cannot see, and therefore cannot strategically direct, the operation it owns. **Horizon 1 must address all four foundational gaps simultaneously** — they cannot be resolved in sequence.

4. Transformation Framework — Three Horizons

4.1 Transformation Vision

“By 2028, Well Land Investment will be the Maldives’ most operationally reliable and trusted heavy-equipment and marine rental operator — known for asset readiness, safety leadership, and transparent service delivery that consistently exceeds client expectations.”

4.2 Three-Horizon Model

The transformation is structured across three sequential but partially overlapping horizons, each building on the foundation established by the previous phase.¹ This approach prevents the common failure of organisations attempting to adopt advanced technologies before their operational foundation is strong enough to generate reliable data and sustain process discipline.

Table 3: Three Transformation Horizons — Well Land Innovation Roadmap

	HORIZON 1 Operational Foundation 0 – 6 Months	HORIZON 2 Digital Intelligence 6 – 18 Months	HORIZON 3 Market Leadership 18 – 36 Months
Primary Focus	Build the operational backbone — processes, governance, measurement	Digitalise and instrument — data, telematics, predictive capability	Differentiate and grow — premium positioning, new service models
Key Deliverables	• Asset class SOPs (all equipment) • KPI register and tracking framework • Pre-mobilisation readiness checklists • Governance structure and reporting lines • Incident and near-miss reporting system	• Fleet telematics pilot (subset of assets) • Condition-based maintenance scheduling • Digital dispatch and handover system • Cloud-based documentation platform • Applied R&D programme governance	• Outcome-based service contracts • Customer Reliability Forum (quarterly) • OEM partnership programme • Premium brand positioning • Business model evolution strategy
Innovation Mode	Closed — proprietary SOPs and safety-critical procedures developed internally	Applied R&D — controlled pilots with clear baselines and go/no-go gates	Open — co-designed with project clients, OEMs, and the market
Primary Risk	Resistance to formalisation from long-serving staff accustomed to informal methods	Technology adoption failure due to insufficient change management investment	Service model changes rejected by clients if not validated through co-design
Success Indicator	100% SOP coverage; KPI dashboard live; governance framework endorsed by board	≥20% reduction in unplanned downtime from pre-telematics baseline	≥2 outcome-based contracts live; CSAT score baseline established and tracked

Source: Adapted from O'Reilly et al. (2013)⁸; March (1991)⁸; Tidd et al. (2021)²

¹Organisational ambidexterity — balancing exploitation and exploration: O'Reilly, C.A. and Tushman, M.L. (2013) Academy of Management Perspectives, 27(4), pp. 324–338; March, J.G. (1991) Organization Science, 2(1), pp. 71–87.

5. Horizon 1 — Operational Foundation (0–6 Months)

Horizon 1 establishes the operational infrastructure that every subsequent investment depends on. It is not glamorous work, but it is the most strategically important phase of the transformation. Without documented SOPs, live KPI data, structured asset readiness protocols, and a functioning governance framework, Well Land cannot make evidence-based decisions, cannot demonstrate its value to clients or the board, and cannot provide the data foundation that digital tools require to function.

Table 4: Horizon 1 — Deliverables Matrix (SOPs, KPIs, Asset Readiness, Governance)

WORKSTREAM	DELIVERABLE	SCOPE	OUTCOME / BENEFIT
SOPs & Standard Procedures	Asset class SOPs Safety & HSE protocols Operator certification matrix	Documented procedures for all heavy plant: cranes, excavators, trailers, barges, tugboats Lifting plans, banksman protocols, stop-the-job authority Version control, review schedule, owner assignment	Eliminates single-point-of-failure knowledge risk Regulatory compliance evidence Faster onboarding; consistent service delivery
KPI Registers & Tracking	KPI framework Monthly dashboard Excel register suite	Asset utilisation %, equipment uptime %, mobilisation response time, incident rate, CSAT Automated calculation logic; monthly board-ready output Linked to asset register, maintenance log, dispatch records	Board visibility into operational performance Data-driven investment decisions Trend identification and early-warning signals
Asset Readiness Framework	Pre-mobilisation checklists Maintenance schedule register Asset readiness ratings	Digital pre-start inspection for each asset class Planned maintenance intervals per OEM specification Traffic-light readiness status (Green / Amber / Red) per asset	Reduction in mobilisation delays Predictive maintenance foundation Client-facing transparency on asset status
Governance Structure & Reporting	Reporting framework Escalation matrix Monthly ops review	Defined reporting lines: operational → GM → Antrac board Clear escalation triggers: safety events, downtime thresholds, client complaints Standardised monthly operational review format	Antrac board has real-time operational visibility Accountability embedded in management structure Platform for Horizon 2 and 3 investment decisions

Source: Operational design, Well Land Investment Pvt Ltd; Neely et al. (1995)⁴; Cooper (1990)⁵

5.1 Standard Operating Procedures

SOPs are the foundation of every other workstream in this transformation. A well-designed SOP does three things simultaneously: it **protects staff** by defining safe working methods; it **protects clients** by ensuring consistent service delivery regardless of who is on shift; and it **protects the business** by creating an auditable

record of compliance. For Well Land, SOPs must be developed at the asset-class level, covering pre-mobilisation inspection, lifting and towage operations, maintenance triggers, incident escalation, and operator handover.²

Critically, SOPs should be developed with — not imposed on — the frontline teams who will use them. Operators and mechanics carry tacit knowledge about equipment behaviour, safety nuances, and failure modes that no manager can fully observe from a distance. Embedding this knowledge into documented procedures converts individual expertise into organisational resilience.

5.2 KPI Registers & Performance Tracking

The KPI framework for Well Land must be designed around operational realities rather than generic metrics. The initial register should track eight core metrics: asset utilisation rate, equipment uptime percentage, mobilisation response time, unplanned downtime events, incident and near-miss rate, SOP compliance rate, customer satisfaction score, and repeat booking/contract renewal rate.³ This suite covers the full performance spectrum: operational efficiency, service reliability, safety, governance, and commercial health.

The KPI dashboard should be designed to produce a board-ready monthly output with no additional preparation time from the GM. This requires building calculation logic directly into the register structure from inception — not retrofitting reporting onto a manual data collection system.

5.3 Asset Readiness Framework

Asset readiness is Well Land's most direct competitive lever. A client choosing between two crane hire operators of equivalent fleet capacity will award the contract to the operator who can guarantee availability, certify operator competence, and evidence compliance. Well Land's asset readiness framework should introduce a traffic-light status system per asset (Green / Amber / Red), digital pre-start checklists per asset class, and a planned maintenance schedule aligned with OEM specifications.⁴

5.4 Governance Structure & Reporting Lines

A governance framework defines how information flows from operations to the board, how decisions are escalated, and how accountability is embedded in the management structure. For Well Land, the framework should establish: a monthly operational review between the GM and Antrac group management; a quarterly board performance presentation using the KPI dashboard; a defined escalation matrix for safety events, significant downtime, and client complaints; and a semi-annual transformation progress review against this roadmap.⁵

²Psychological safety and team learning: Edmondson, A. (1999) Administrative Science Quarterly, 44(2), pp. 350–383; Anderson, N. et al. (2014) Journal of Management, 40(5), pp. 1297–1333.

³Performance measurement in asset-intensive environments: Neely, A., Gregory, M. and Platts, K. (1995) Int. Journal of Operations and Production Management, 15(4), pp. 80–116; Bititci, U. et al. (2012) Int. Journal of Management Reviews, 14(3), pp. 305–327.

⁴IoT and telematics in asset-intensive industries: Tidd, J. and Bessant, J. (2021) Managing Innovation, 7th edn. Wiley. ISBN 978-1-119-71330-2.

⁵Stakeholder theory and innovation: Donaldson, T. and Preston, L.E. (1995) Academy of Management Review, 20(1), pp. 65–91; Mitchell, R.K. et al. (1997) Academy of Management Review, 22(4), pp. 853–886.

6. Horizon 2 — Digital Intelligence (6–18 Months)

Horizon 2 transforms Well Land from a data-aware operation into a **data-driven operation**. The distinction is significant: data-aware organisations collect KPIs; data-driven organisations use real-time operational data to make predictive decisions before problems occur. This transition is enabled by three interconnected investments: fleet telematics, digital dispatch, and an applied R&D programme governance structure.⁶

6.1 Fleet Telematics Pilot

Fleet telematics — the real-time monitoring of engine hours, fuel consumption, fault codes, idle time, and location data — is the single highest-leverage technology investment available to Well Land at its current stage of maturity. The case for telematics is not theoretical: operators in analogous asset-intensive environments consistently demonstrate 15–25% reductions in unplanned downtime following telematics adoption, driven by condition-based maintenance replacing time-interval maintenance.

Well Land should initiate a controlled pilot on 3–5 assets representing different asset classes, with a defined 90-day trial period, a clear baseline downtime rate established from Horizon 1 KPI data, and an explicit go/no-go decision gate before fleet-wide commitment. This disciplined approach — hypothesis before investment, evidence before scale — is the architectural principle that distinguishes a managed innovation programme from a technology spending exercise.

6.2 Digital Dispatch & Documentation

Parallel to telematics, Well Land should digitise its dispatch and documentation workflow. Currently, mobilisation coordination, operator assignment, client communication, and job completion records are managed through informal channels. This creates four simultaneous risks: communication failures causing mobilisation delays; absence of evidence in client disputes; inability to analyse dispatch patterns for efficiency improvements; and compliance exposure should a safety incident require documentary evidence of pre-mobilisation checks.

6.3 Applied R&D Programme Governance

By Month 12, Well Land will have sufficient operational data — from the H1 KPI register and the telematics pilot — to identify the next tier of improvement opportunities. Formalising an Applied R&D programme governance structure means establishing a dedicated quarterly innovation review where operational data is translated into improvement hypotheses, and those hypotheses are entered into the five-stage innovation pipeline described in Section 8.⁷

⁷ Stage-gate model for innovation process management: Cooper, R.G. (1990) *Business Horizons*, 33(3), pp. 44–54; Crossan, M.M. and Apaydin, M. (2010) *Journal of Management Studies*, 47(6), pp. 1154–1191.

7. Horizon 3 — Market Leadership (18–36 Months)

Horizon 3 translates operational excellence into market differentiation. By Month 18, Well Land will have structured processes, live KPI data, and digital operational capability. The strategic question at that point is: how does Well Land use this capability to capture a greater share of the Maldivian infrastructure market and command premium pricing? The answer lies in **service innovation**: restructuring the value proposition from commodity asset access to guaranteed operational outcomes.⁸

7.1 Outcome-Based Service Contracts

The most significant commercial innovation available to Well Land in Horizon 3 is the introduction of availability-linked and uptime-guaranteed service agreements. Rather than charging a daily hire rate for access to an asset, Well Land commits to a defined level of operational performance — such as **95% equipment availability across a project's duration** — and prices accordingly. This shifts competition from rate-card comparison to demonstrated reliability, a dimension on which Well Land — with its formalised SOPs, telematics data, and maintenance records — will be able to make credible commitments that competitors cannot match.

7.2 Customer Reliability Forum

A quarterly Customer Reliability Forum operationalises the principle of open innovation with clients.⁹ Rather than waiting for complaints to surface informally, Well Land proactively convenes its most strategic project clients to review mobilisation performance data, surface pain points, and jointly identify service improvements. This converts clients from evaluators into co-designers, fundamentally changing the nature of the commercial relationship. Clients who have shaped a service are far less likely to defect to a competitor on price alone.

7.3 OEM Partnership Programme

Well Land's ability to maintain fleet reliability at scale depends significantly on the quality of its relationships with Original Equipment Manufacturers. A structured OEM partnership programme — built on regular technical reviews, access to updated diagnostic software and maintenance protocols, and joint pilot programmes for new maintenance approaches — converts the supplier relationship from transactional to collaborative. The strategic benefit is absorptive capacity¹⁰: the faster Well Land can integrate OEM technical knowledge into its own maintenance practices, the more rapidly it improves fleet reliability without proportional cost increases.

⁸ Outcome-based service logic and service-dominant logic: Vargo, S.L. and Lusch, R.F. (2004) *Journal of Marketing*, 68(1), pp. 1–17; Ostrom, A.L. et al. (2010) *Journal of Service Research*, 13(1), pp. 4–36.


⁹ Open innovation and external knowledge integration: Chesbrough, H. and Crowther, A.K. (2006) *R&D Management*, 36(3), pp. 229–236; West, J. and Bogers, M. (2014) *Journal of Product Innovation Management*, 31(4), pp. 814–831.

¹⁰ Absorptive capacity and knowledge transfer: Cohen, W.M. and Levinthal, D.A. (1990) *Administrative Science Quarterly*, 35(1), pp. 128–152; Zahra, S.A. and George, G. (2002) *Academy of Management Review*, 27(2), pp. 185–203.

8. Innovation Governance — The Five-Stage Pipeline

Sustainable transformation requires a structured process for generating, evaluating, and scaling improvements on a continuous basis. Well Land’s innovation programme should be governed through a **five-stage pipeline** that moves every improvement initiative from idea to impact through disciplined, evidence-based gates.¹¹ This prevents the two most common failure modes: pursuing ideas that are interesting but strategically irrelevant, and scaling pilots that have not been properly validated.

Figure 2: Well Land Investment — Five-Stage Innovation Pipeline

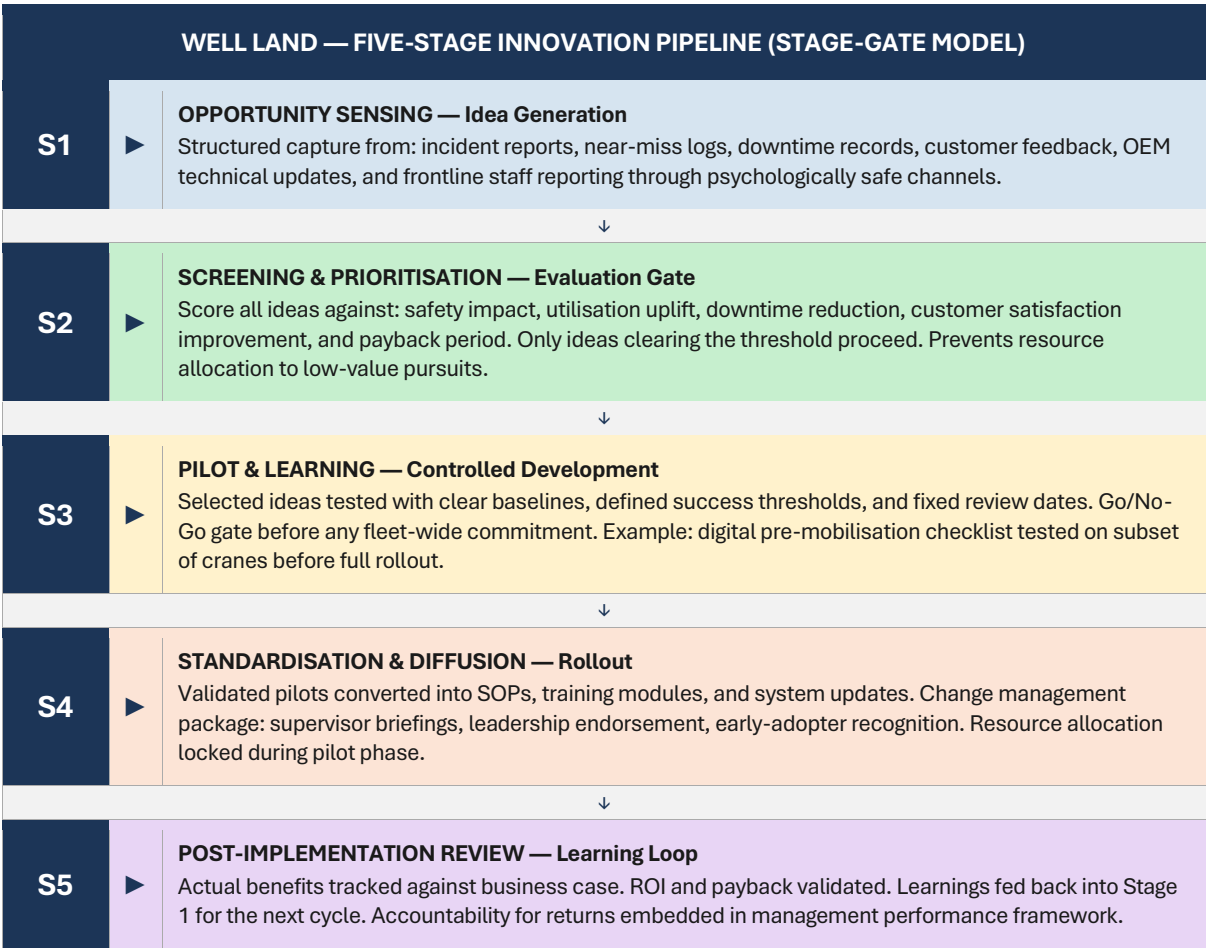

Source: Adapted from Cooper (1990)⁵; Crossan et al. (2010)⁵; Edmondson (1999)⁶

8.1 Stakeholder Roles in the Innovation Process

The pipeline functions effectively only when the right stakeholders are engaged at each stage. The GM Logistics owns the pipeline architecture and gates. Frontline operators and mechanics are the primary idea generators at Stage 1 — their proximity to operational reality makes them the most valuable source of practical improvements.¹² Project clients contribute at Stage 2 through the Customer Reliability Forum. OEMs

contribute at Stage 2 and Stage 3 through technical reviews. The Antrac board validates strategic alignment at Stage 2 and receives ROI reporting at Stage 5.

8.2 Managing Change Resistance

In operationally conservative environments, the human dimension of change is consistently the most difficult to manage and the most consequential if mishandled.¹³ For Well Land, resistance will be most pronounced at two transition points: the introduction of formalised SOPs (which some experienced operators will perceive as a challenge to their autonomy and expertise) and the deployment of telematics (which some staff may interpret as surveillance). Both concerns are legitimate and must be addressed directly through transparency, co-design, and visible recognition of the value that frontline expertise brings to the transformation programme.

¹³Managing change resistance: Kotter, J.P. (1996) Leading Change. Harvard Business School Press; Jansen, J.J.P. et al. (2006) Management Science, 52(11), pp. 1661–1674.

9. Performance Measurement Framework

A transformation programme of this scale must be managed against a clear, consistent, and board-visible measurement architecture.¹⁴ Well Land's KPI framework is designed around three measurement dimensions that together tell a complete story of operational health: financial value capture (are we generating returns?), customer value delivery (are we satisfying clients?), and innovation pipeline health (are we building future capability?). The dashboard below defines the eight primary KPIs, their measurement approach, Horizon 1 targets, and strategic significance.

Table 5: Well Land Investment — KPI Performance Dashboard Framework

KPI METRIC	CATEGORY	MEASUREMENT FREQUENCY	TARGET (HORIZON 1)	STRATEGIC IMPORTANCE
Asset Utilisation Rate (%)	Operational Efficiency	Monthly	Establish baseline → improve 10% in H2	Core revenue driver — idle assets are a direct margin cost
Equipment Uptime (%)	Reliability	Monthly	≥92% per asset class	Primary client satisfaction driver; basis for uptime guarantee contracts
Mobilisation Response Time	Service Delivery	Per deployment	Define baseline in M1-2; reduce 15% by end H1	Key differentiator vs. competitors; determines client repeat rate
Unplanned Downtime Events	Maintenance / Reliability	Monthly	Track & reduce — target 25% reduction in H2	Direct revenue loss indicator; predictive maintenance ROI proof point
Incident & Near-Miss Rate	Safety & Compliance	Monthly	Zero lost-time incidents	Regulatory compliance; insurance risk management; operator trust
SOP Compliance Rate (%)	Governance	Bi-monthly audit	100% coverage; ≥95% compliance	Operational foundation integrity; prerequisite for all Horizon 2 investment
Customer Satisfaction (CSAT)	Client Value	Per project completion	Establish baseline in H1; target ≥4.0/5.0 in H2	Market positioning; repeat booking rate; basis for outcome-based contracts
Repeat Booking / Renewal Rate	Commercial	Quarterly	Establish baseline; target ≥70% in H2	Revenue stability; relationship capital; premium positioning proof

Source: Adapted from Neely et al. (1995)⁴; Bititci et al. (2012)⁴; Zeithaml et al. (1996)¹¹; Franco-Santos et al. (2012)

The single most important governance commitment the board can make is to **adopt the KPI dashboard as a standing agenda item** at every quarterly board meeting from Month 3 onward. This signal — that performance data matters at the highest level of the organisation — cascades directly into operational management behaviour and accelerates the culture change that the transformation programme depends on.

10. Transformation Roadmap — 36-Month Timeline

The timeline below provides a programme-level view of all initiatives across the three horizons. Horizon 1 workstreams run concurrently and must be completed before Horizon 2 technology investments are committed. Horizon 3 initiatives begin in Month 10 with the Customer Reliability Forum, which is deliberately initiated before formal Horizon 3 to ensure client intelligence informs the service model design process.

Figure 3: Well Land Investment — 36-Month Transformation Roadmap

WORKSTREAM / INITIATIVE	M1-2	M3-4	M5-6	M7-9	M10-12	M13-18	M19-24	M25-36
HORIZON 1 — Operational Foundation								
SOP Development (all asset classes)								
KPI Register & Dashboard								
Asset Readiness Checklists								
Governance & Reporting Framework								
Incident & Near-Miss System								
HORIZON 2 — Digital Intelligence								
Fleet Telematics Pilot								
Condition-Based Maintenance System								
Digital Dispatch & Documentation								
Applied R&D Programme Governance								
HORIZON 3 — Market Leadership								
Outcome-Based Contract Development								
Customer Reliability Forum								
OEM Partnership Programme								
Premium Service Brand Launch								

Source: Author's strategic programme design; Well Land Investment Pvt Ltd, 2026

11. Risk Register — Transformation Programme

The following risk register identifies the six primary risks to successful delivery of this transformation programme, with likelihood and impact assessments, root cause analysis, and mitigation strategies. The board is advised to review this register quarterly and request GM reporting on any risks that have materialised or escalated since the previous review.

Table 6: Transformation Programme Risk Register

RISK	LIKELIHOOD	IMPACT	ROOT CAUSE	MITIGATION STRATEGY
Staff resistance to SOP formalisation	High	High	Long-serving operators confident in informal methods; fear of accountability	Co-design SOPs with frontline teams; explain rationale; celebrate early adopters; pilot before mandate
KPI baseline unavailable (no historical data)	High	Medium	Operations were not previously tracked; records may be absent or incomplete	Establish M1 as baseline month; build forward; use industry benchmarks for initial targets
Telematics adoption failure (H2)	Medium	High	Insufficient change management; technology not suited to Maldivian conditions or fleet age	Pilot on 2-3 assets first; involve operators in selection; validate OEM compatibility before fleet-wide commitment
Short-term productivity loss during transformation	Medium	Medium	Training time, documentation effort, and process changes divert operational bandwidth	Phase changes to low-demand periods; use protected improvement time; GM provides visible air cover for teams
Board under-investment in Horizon 2	Medium	High	Transformation perceived as operational overhead rather than strategic investment	H1 KPI dashboard demonstrates ROI of foundation investment; business case for H2 built from H1 data
Client reluctance to adopt outcome-based contracts (H3)	Low	Medium	Unfamiliarity with SLA structures; preference for familiar time-based hire	Introduce hybrid model first; co-design with receptive clients; pilot with 1-2 flagship relationships

Source: Operational risk assessment, Well Land Investment Pvt Ltd, 2026; Kotter (1996)¹⁰

12. Strategic Recommendations to the Board

The following six recommendations are presented for board endorsement. Each is directly actionable, assigns clear accountability, and is sequenced to deliver maximum strategic impact in the near term while building the foundation for longer-term transformation.

Table 7: Strategic Recommendations — Board Action Summary

#	RECOMMENDATION	RATIONALE	FIRST ACTION
1	Endorse and resource the Horizon 1 Operational Foundation programme immediately	All Horizon 2 and 3 investments depend on structured processes, governance, and data — without H1, digital tools will fail to deliver their promised returns	Board resolution to allocate H1 budget; appoint workstream owners by role; set 6-month milestone review
2	Approve the KPI dashboard as the primary board reporting mechanism	Replaces informal verbal updates with data-driven governance; enables trend identification and investment justification	GM Logistics to deliver first dashboard by end of Month 2; board to adopt as standing agenda item
3	Commit to a fleet telematics pilot in Horizon 2 — no later than Month 9	Telematics is the highest single-leverage investment available — condition-based maintenance directly reduces the largest operational cost: unplanned downtime	Commission OEM-compatible telematics options assessment in M4-5; allocate pilot budget in H1 board review
4	Mandate psychological safety as an operational principle — not an HR initiative	Frontline operators and mechanics hold the highest-fidelity knowledge about equipment and safety risks — this knowledge must flow upward consistently	GM Logistics to establish near-miss reporting protocol and team briefing norm by end of Month 1
5	Initiate the first Customer Reliability Forum no later than Month 10	Client co-design prevents the common failure of building innovations clients do not value — early engagement converts clients from evaluators to collaborators	GM Logistics to identify 2-3 flagship client contacts; send forum invitation in M8
6	Position Well Land as Antrac's reliability and governance flagship — not just a fleet asset	Formalised operations, published SOPs, and a live KPI dashboard signal to the Maldivian market that Well Land operates to a higher standard than its competitors	Well Land branding and capability statement updated following H1 completion; shared with Antrac marketing team

Source: Author's strategic advisory, Well Land Investment Pvt Ltd, March 2026

12.1 On Investment & Resources

The Horizon 1 programme is primarily a human capital and management time investment, not a capital expenditure programme. The largest cost is the protected management bandwidth required to design, document, and deploy the SOP library, KPI register, and governance framework in parallel with ongoing operations. The board should authorise the GM to ring-fence up to 20% of working hours for transformation

activities during the six-month foundation phase, without this being interpreted as a reduction in operational accountability.

Horizon 2 investments — particularly telematics and digital dispatch — will require capital expenditure. The business case for these investments will be constructed from Horizon 1 KPI baseline data, ensuring that technology commitments are justified by evidence rather than aspiration. The board should set a Horizon 2 budget envelope at the six-month H1 review, informed by the baseline data that will by then be available.

12.2 On Timeline & Accountability

This roadmap is ambitious but achievable within the stated timeline if two conditions are met: visible board-level endorsement of the transformation programme, communicated directly to Well Land staff; and consistent operational air cover from the GM during the disruptive early phases of Horizon 1. Transformation programmes that lack one or both of these conditions consistently fall behind schedule or fail to embed permanently.

CLOSING STATEMENT

Well Land Investment is at an inflection point. The operational context — a growing Maldivian infrastructure market, rising client sophistication, and available digital tools — creates a genuine first-mover opportunity for a heavy equipment operator willing to invest in structured improvement before competitive pressure makes it unavoidable.

The transformation programme presented in this report is designed to be **practical, phased, and evidence-driven** — starting with the unglamorous but essential work of building operational foundations, then layering digital capability, and finally achieving market differentiation through service excellence. At every stage, the investment is justified by the data from the previous stage.

The board's role in this programme is not merely to approve a budget. It is to signal, unambiguously, that operational excellence is a strategic priority for Antrac Holding Group — and that Well Land Investment is the vehicle through which that priority will be demonstrated to the Maldivian market.

Ali Mushthaq Ibrahim

General Manager — Logistics (Well Land Operations)

Well Land Investment Pvt Ltd | Antrac Holding Group

March 2026

SUPPORTING ACADEMIC REFERENCES

The strategic recommendations in this report are underpinned by peer-reviewed scholarship in innovation management, performance measurement, and organisational transformation. Key sources are cited as footnotes throughout the report and listed in full below.

- Anderson, N., Potočník, K. and Zhou, J. (2014) 'Innovation and creativity in organizations', *Journal of Management*, 40(5), pp. 1297–1333. Available at: https://www.researchgate.net/publication/260275534_Innovation_and_Creativity_in_Organizations_A_State-of-the-Science_Review_Prospective_Commentary_and_Guiding_Framework
- Antrac Holding Pvt Ltd (n.d.a) About us. Available at: <https://antracholding.com/about-us/> (Accessed: 15 April 2026).
- Antrac Holding Pvt Ltd (n.d.b) Company milestones. Available at: <https://antracholding.com/company-milestones/> (Accessed: 15 April 2026).
- Antrac Holding Pvt Ltd (n.d.c) Rental services. Available at: <https://antracholding.com/portfolio/rental-services/> (Accessed: 15 April 2026).
- Barney, J. (1991) 'Firm resources and sustained competitive advantage', *Journal of Management*, 17(1), pp. 99–120. Available at: <https://doi.org/10.1177/014920639101700108>
- Bititci, U., Garengo, P., Dörfler, V. and Nudurupati, S. (2012) 'Performance measurement: Challenges for tomorrow', *International Journal of Management Reviews*, 14(3), pp. 305–327. Available at: <https://doi.org/10.1111/j.1468-2370.2011.00318.x>
- Chesbrough, H. and Crowther, A.K. (2006) 'Beyond high tech: Early adopters of open innovation', *R&D Management*, 36(3), pp. 229–236. Available at: <https://doi.org/10.1111/j.1467-9310.2006.00428.x>
- Cohen, W.M. and Levinthal, D.A. (1990) 'Absorptive capacity', *Administrative Science Quarterly*, 35(1), pp. 128–152. Available at: <https://doi.org/10.2307/2393553>
- Cooper, R.G. (1990) 'Stage-gate systems', *Business Horizons*, 33(3), pp. 44–54. Available at: [https://doi.org/10.1016/0007-6813\(90\)90040-I](https://doi.org/10.1016/0007-6813(90)90040-I)
- Crossan, M.M. and Apaydin, M. (2010) 'A multi-dimensional framework of organizational innovation', *Journal of Management Studies*, 47(6), pp. 1154–1191. Available at: <https://doi.org/10.1111/j.1467-6486.2009.00880.x>
- Damanpour, F. (1991) 'Organizational innovation: A meta-analysis', *Academy of Management Journal*, 34(3), pp. 555–590. Available at: <https://journals.aom.org/doi/abs/10.5465/256406>
- Donaldson, T. and Preston, L.E. (1995) 'The stakeholder theory of the corporation', *Academy of Management Review*, 20(1), pp. 65–91. Available at: <https://doi.org/10.5465/amr.1995.9503271992>
- Edmondson, A. (1999) 'Psychological safety and learning behavior in work teams', *Administrative Science Quarterly*, 44(2), pp. 350–383. Available at: <https://doi.org/10.2307/2666999>
- Franco-Santos, M., Lucianetti, L. and Bourne, M. (2012) 'Contemporary performance measurement systems', *Management Accounting Research*, 23(2), pp. 79–119. Available at: <https://doi.org/10.1016/j.mar.2012.04.001>
- Jansen, J.J.P., Van Den Bosch, F.A.J. and Volberda, H.W. (2006) 'Exploratory innovation, exploitative innovation, and performance', *Management Science*, 52(11), pp. 1661–1674. Available at: <https://doi.org/10.1287/mnsc.1060.0576>
- Kotter, J.P. (1996) *Leading change*. Boston: Harvard Business School Press. Available at: [https://books.google.mv/books?hl=en&lr=&id=xpGX1EWL_EMC&oi=fnd&pg=PR7&dq=Kotter,+J.P.+\(1996\)+Leading+change.+Boston&ots=Te_4KmPqHx&sig=pBbFGx-fxfcBQsl91kQ92hkOFqM&redir_esc=y#v=onepage&q&f=false](https://books.google.mv/books?hl=en&lr=&id=xpGX1EWL_EMC&oi=fnd&pg=PR7&dq=Kotter,+J.P.+(1996)+Leading+change.+Boston&ots=Te_4KmPqHx&sig=pBbFGx-fxfcBQsl91kQ92hkOFqM&redir_esc=y#v=onepage&q&f=false)
- March, J.G. (1991) 'Exploration and exploitation in organizational learning', *Organization Science*, 2(1), pp. 71–87. Available at: <https://doi.org/10.1287/orsc.2.1.71>
- Mitchell, R.K., Agle, B.R. and Wood, D.J. (1997) 'Toward a theory of stakeholder identification and salience', *Academy of Management Review*, 22(4), pp. 853–886. Available at: <https://doi.org/10.5465/amr.1997.9711022105>
- Neely, A., Gregory, M. and Platts, K. (1995) 'Performance measurement system design', *International Journal of Operations and Production Management*, 15(4), pp. 80–116. Available at: <https://doi.org/10.1108/01443579510083622>

- Nonaka, I. (1994) 'A dynamic theory of organizational knowledge creation', *Organization Science*, 5(1), pp. 14–37. Available at: <https://doi.org/10.1287/orsc.5.1.14>
- O'Reilly, C.A. and Tushman, M.L. (2013) 'Organizational ambidexterity', *Academy of Management Perspectives*, 27(4), pp. 324–338. Available at: <https://doi.org/10.5465/amp.2013.0025>
- Ostrom, A.L. et al. (2010) 'Moving forward and making a difference', *Journal of Service Research*, 13(1), pp. 4–36. Available at: <https://doi.org/10.1177/1094670509357611>
- Parasuraman, A., Zeithaml, V.A. and Berry, L.L. (1988) 'SERVQUAL', *Journal of Retailing*, 64(1), pp. 12–40. Available at: https://www.researchgate.net/publication/200827786_SERVQUAL_A_Multiple-Item_Scale_for_Measuring_Consumer_Perceptions_of_Service_Quality
- Teece, D.J. (2010) 'Business models, business strategy and innovation', *Long Range Planning*, 43(2–3), pp. 172–194. Available at: <https://doi.org/10.1016/j.lrp.2009.07.003>
- Teece, D.J., Pisano, G. and Shuen, A. (1997) 'Dynamic capabilities and strategic management', *Strategic Management Journal*, 18(7), pp. 509–533. Available at: [https://doi.org/10.1002/\(SICI\)1097-0266\(199708\)18:7<509::AID-SMJ882>3.0.CO;2-Z](https://doi.org/10.1002/(SICI)1097-0266(199708)18:7<509::AID-SMJ882>3.0.CO;2-Z)
- Tidd, J. and Bessant, J. (2021) *Managing innovation: Integrating technological, market and organizational change*. 7th edn. Chichester: Wiley. ISBN: 978-1-119-71330-2. Available at: <https://www.wiley.com/en-us/Managing+Innovation:+Integrating+Technological,+Market+and+Organizational+Change,+7th+Edition-p-9781119713302>
- Vargo, S.L. and Lusch, R.F. (2004) 'Evolving to a new dominant logic for marketing', *Journal of Marketing*, 68(1), pp. 1–17. Available at: <https://doi.org/10.1509/jmkg.68.1.1.24036>
- West, J. and Bogers, M. (2014) 'Leveraging external sources of innovation', *Journal of Product Innovation Management*, 31(4), pp. 814–831. Available at: <https://doi.org/10.1111/jpim.12125>
- Zahra, S.A. and George, G. (2002) 'Absorptive capacity: A review, reconceptualization, and extension', *Academy of Management Review*, 27(2), pp. 185–203. Available at: <https://journals.aom.org/doi/10.5465/amr.2002.6587995>
- Zeithaml, V.A., Berry, L.L. and Parasuraman, A. (1996) 'The behavioral consequences of service quality', *Journal of Marketing*, 60(2), pp. 31–46. Available at: <https://doi.org/10.1177/002224299606000203>
